

SOLICITATION NUMBER: NAIP-TO-3-12-1

TASK ORDER REQUEST FOR PROPOSAL

U.S. Department of Agriculture (USDA)
NATIONAL AGRICULTURE IMAGERY PROGRAM (NAIP)

BASE YEAR

Solicitation Issue Date: February 1, 2012



U.S. DEPARTMENT OF AGRICULTURE
FARM SERVICE AGENCY
AERIAL PHOTOGRAPHY FIELD OFFICE

NOTICE TO OFFEROR

Any proposal submitted for this RFP must be identified with the following information labeled on the outside of the mailing package:

SOL.NO: NAIP-TO-3-12-1
DUE DATE: MARCH 2, 2012, 4:30 PM
RECEIVING OFFICE: CONTRACTING

Mail To: AERIAL PHOTOGRAPHY FIELD OFFICE
CONTRACTING OFFICER
2222 WEST 2300 SOUTH
SALT LAKE CITY UTAH 84119-2020

NOTICE TO OFFERORS:

This Task Order RFP solicitation is for the Base Year, covering the 2012 performance period, under the multi-award fixed-price IDIQ NAIP contract. Prospective contractors are instructed to submit a single proposal in response to this task order solicitation and the contract solicitation AG-8447-S-12-0001. Proposals will be evaluated based on the combined response to both documents. Contracts will be awarded prior to award of any task orders. Task orders are the method by which project item areas are awarded. See Section L of the contract for proposal preparation instructions.

Proposals must be presented in two parts: a pricing proposal and a technical proposal. Two complete printed copies of the entire proposal are required. The pricing proposal shall contain two signed documents, the contract form SF-33 (page 1 of the IDIQ contract RFP), and the task order pricing proposal (pages 1-3 of the task order RFP). Please do not secure your proposal using a "plastic comb" or spiral type bindings, and limit the size to a maximum of 100 double-sided, letter sized pages (camera reports and documents may be placed in separate volume without page limitations). Task order awards will be made based on procedures established in Section L-3, Paragraph 3.2 of the contract RFP.

Contractors proposing states with restricted airspace areas are required to provide detail explanations on how they plan on acquiring imagery in those areas. The explanation should include discussions on airspace clearance, possible DoD imagery review, alternate acquisition approaches, and potential impacts to delivery schedule.

Contractors are requested to identify in their technical proposals any prospective or known secondary contract requirements. If the requirement may add risk in completing this Task Order on time, please describe in your proposal how you plan on minimizing the risk. The Government expects all NAIP acquisition and delivery schedules to be on time and failure due to increased risk may be reason for terminating the contract for default.

PLEASE NOTE: The Government's obligation under this task order RFP is contingent upon the availability of funds from which payment for contract purposes can be made. No legal liability on the part of the Government for any payment, other than the minimum guaranteed amount, may arise until funds are made available to the Contracting Officer for all or part of the task order requirements. See Paragraph 4.4 of the task order.

TASK ORDER REQUEST FOR PROPOSAL

PART I – PRICING PROPOSAL

NATIONAL AGRICULTURE IMAGERY PROGRAM

1.0 AERIAL PHOTOGRAPHY AND DIGITAL IMAGERY SERVICES

Furnish aerial photography and all related services and supplies in accordance with the requirements, specifications, terms, conditions, clauses, and provisions specified herein and in the original indefinite-delivery, indefinite-quantity (IDIQ) contract, effective for the periods stated in the schedule. The Government’s proposed project areas, quantities, and other parameters listed in Paragraphs 1.2, Proposed Project Item Areas and Quantities, and 2.1, General Requirements, are subject to change through the negotiation process of selecting the “Best Value” source for task order award.

1.1 Pricing Proposal

In the spaces provided, please indicate your company’s name and authorized signature, quantities of digital orthoimagery quarter quadrangles (DOQQ) for imagery acquisition and digital image processing, unit prices, and extended total amounts consistent with the state(s) you are offering.

2012 NATIONAL AGRICULTURE IMAGERY PROGRAM (NAIP)				
COMPANY NAME:			AUTHORIZED SIGNATURE:	
DESCRIPTION	QTY.	UNIT	AVG UNIT PRICE	TOTAL AMOUNT
1m Orthorectified Imagery (One meter GeoTIFF files)		DOQQ		
<u>PRICING PROPOSAL INSTRUCTIONS:</u>				
<p>Indicate the state(s) proposed in your offer in the table at Paragraph 1.2 below, and enter the cumulative values in the space provided above. Please ensure that the total amount can be calculated by multiplying the quantity times the average unit price. If your proposal includes adjoining states with the same photographic periods, duplicate DOQQs along the boundary will be eliminated from the total quantity during final task order award negotiations.</p> <p>Please note that in the table at paragraph 1.2, each state has been prioritized (1=high to 3=lowest) to determine the order of awards based on final funding levels. A high priority state is likely to be considered for an award, where a low priority state may not. State priorities should be used for your proposal planning purposes. The Government reserves the right to select any state or area for award independent of the stated priority.</p>				

1.2 Proposed Project Item Areas and Quantities

In the proposed project item areas list, please mark the appropriate space provided (CHECK BOX) next to the state(s) you are offering in your proposal, enter the unit price, and calculated extended price. **PLEASE NOTE: The minimum unit of offer is a project item area listed below, by state, including all required imagery within that state or area.**

CHECK BOX	STATE	FSA PRIORITY*	QUARTER QUADS	UNIT PRICE	EXTENDED PRICE
[]	Alabama	3	3,482		
[]	Arizona	2	7,629		
[]	Arkansas	3	3,600		
[]	California	1	11,095		
[]	Colorado	3	7,423		
[]	Connecticut	2	412		
[]	Delaware	3	176		
[]	Florida	2	3,954		
[]	Georgia	3	3,913		
[]	Idaho	3	6,554		
[]	Illinois	1	4,131		
[]	Indiana	2	2,689		
[]	Iowa	2	4,239		
[]	Kansas	2	5,902		
[]	Kentucky	2	2,930		
[]	Louisiana	3	3,283		
[]	Maine	2	2,748		
[]	Maryland	3	906		
[]	Massachusetts	2	744		
[]	Michigan	1	4,844		
[]	Minnesota	2	6,791		
[]	Mississippi	1	3,237		
[]	Missouri	1	5,018		
[]	Montana	3	11,776		
[]	Nebraska	1	5,625		
[]	Nevada	2	7,454		
[]	New Hampshire	2	771		
[]	New Jersey	2	636		
[]	New Mexico	3	8,028		
[]	New York	2	3,880		
[]	North Carolina	1	3,581		
[]	North Dakota	3	5,712		
[]	Ohio	3	3,049		
[]	Oklahoma	2	4,815		
[]	Oregon	1	7,466		
[]	Pennsylvania	2	3,343		
[]	Rhode Island	2	116		
[]	South Carolina	3	2,154		

[]	South Dakota	2	5,992		
[]	Tennessee	2	3,000		
[]	Texas	1	17,277		
[]	Utah	3	6,032		
[]	Vermont	2	812		
[]	Virginia	1	3,029		
[]	Washington	3	5,718		
[]	West Virginia	3	1,831		
[]	Wisconsin	2	4,484		
[]	Wyoming	1	7,357		

Legend: * Designates FSA’s priority for planning purposes only. Depending on funding levels, states may be awarded in different priority groups that best meets the Government’s needs.

1.3 Delivery Schedule

All delivery materials required under the NAIP task order shall be delivered on or before the dates listed in the table below. DOQQ delivery dates are 30 days after the end of the acquisition period and CCM delivery dates are 45 days after the acquisition period. The Contractor shall maintain a copy of the digital data until APFO acknowledges receipt. The Government **strongly encourages** the Contractor to submit any/all DOQQs when available and not wait for a “complete set” prior to submission. This incremental approach will allow the Government to inspect the data more efficiently and provide a timelier acceptance/rejection response to the Contractor.

STATE	DOQQ DELIVERY	CCM DELIVERY
Alabama	15 Oct 11	30 Oct 12
Arizona	30 Sep 11	15 Oct 12
Arkansas	15 Oct 11	30 Oct 12
California		
Season 1	30 Jun 12	15 Jul 12
Season 2	30 Jul 12	14 Aug 12
Season 3	30 Aug 12	14 Sep 12
Season 4	6 Sep 12	21 Sep 12
Colorado		
Season 1	14 Sep 12	29 Sep 12
Season 2	15 Oct 12	30 Oct 12
Connecticut	14 Sep 11	29 Sep 12
Delaware	14 Sep 11	29 Sep 12
Florida		
Season 1	30 Jul 12	14 Aug 12
Season 2	30 Jul 12	14 Aug 12
Season 3	30 Nov 12	15 Dec 12
Georgia	1 Oct 11	16 Oct 12
Idaho	14 Sep 11	29 Sep 12
Illinois		
Season 1	14 Aug 12	29 Aug 12
Season 2	30 Aug 12	14 Sep 12
Indiana	14 Sep 11	29 Sep 12

STATE	DOQQ DELIVERY	CCM DELIVERY
Iowa	15 Oct 11	30 Oct 12
Kansas		
Season 1	6 Sep 12	21 Sep 12
Season 2	1 Oct 12	16 Oct 12
Kentucky	14 Sep 11	29 Sep 12
Louisiana	30 Aug 11	14 Sep 12
Maine	15 Oct 11	30 Oct 12
Maryland	14 Sep 11	29 Sep 12
Massachusetts	30 Sep 11	15 Oct 12
Michigan	11 Sep 11	26 Sep 12
Minnesota	30 Sep 11	15 Oct 12
Mississippi	30 Sep 11	15 Oct 12
Missouri	30 Aug 11	14 Sep 12
Montana		
Season 1	14 Aug 12	29 Aug 12
Season 2	24 Aug 12	8 Sep 12
Season 3	4 Sep 12	19 Sep 12
Season 4	14 Sep 12	29 Sep 12
Nebraska	30 Sep 11	15 Oct 12
Nevada	31 Aug 11	15 Sep 12
New Hampshire	30 Sep 11	15 Oct 12
New Jersey	30 Sep 11	15 Oct 12

STATE	DOQQ DELIVERY	CCM DELIVERY
New Mexico	14 Sep 11	29 Sep 12
New York	30 Oct 11	14 Nov 12
North Carolina	14 Sep 11	29 Sep 12
North Dakota	19 Sep 11	4 Oct 12
Ohio	1 Oct 11	16 Oct 12
Oklahoma		
Season 1	15 Jul 12	30 Jul 12
Season 2	30 Oct 12	14 Nov 12
Oregon		
Season 1	30 Aug 12	14 Sep 12
Season 2	14 Sep 12	29 Sep 12
Pennsylvania	30 Oct 11	14 Nov 12
Rhode Island	14 Sep 11	29 Sep 12
South Carolina	31 Jul 11	15 Aug 12
South Dakota	30 Sep 11	15 Oct 12
Tennessee		
Season 1	15 Oct 12	30 Oct 12
Season 2	15 Oct 12	30 Oct 12

STATE	DOQQ DELIVERY	CCM DELIVERY
Texas		
Season 1	15 Jul 12	30 Jul 12
Season 2	30 Aug 12	14 Sep 12
Season 3	30 Sep 12	15 Oct 12
Season 4	30 Oct 12	14 Nov 12
Utah	14 Sep 11	29 Sep 12
Vermont	30 Sep 11	15 Oct 12
Virginia		
Season 1	14 Sep 12	29 Sep 12
Season 2	14 Sep 12	29 Sep 12
Washington		
Season 1	30 Aug 12	14 Sep 12
Season 2	14 Sep 12	29 Sep 12
Season 3	15 Oct 12	30 Oct 12
West Virginia	30 Oct 11	14 Nov 12
Wisconsin	30 Sep 11	15 Oct 12
Wyoming	14 Sep 11	29 Sep 12

1.4 Task Order Performance Period

The task order performance period for the acquisition and delivery of NAIP imagery in the Base Year 2012 is: **Date of Award through December 31, 2012.**

1.5 Photographic Periods

The photographic period for each project item area is listed in Paragraph 2.1, General Requirements. Several project item areas have multiple seasons (see Attachment 2, State Coverage Maps, for detail information on multiple season dates). It shall be the Contractor's responsibility to properly flight plan each area to acquire all imagery within the designated period.

2.0 PROJECT REQUIREMENTS

2.1 General Requirements

(a) The following task order deliverables shall be prepared and submitted by the Contractor:

- (1) Quarter Quadrangle Image Tiles
- (2) Compressed County Mosaics (CCMs)
- (3) Accuracy and Quality Control Reports
- (4) Progress Reports
- (5) Metadata and other text files

- (b) All materials shall be prepared in accordance with IDIQ contract specifications and work statement (Section C), packaging and marking (Section D), inspection and acceptance (Section E), and delivery schedule (Section F) requirements.
- (c) A product warranty shall be provided on all deliverables in accordance with Section I-8, Warranty of Supplies of a Noncomplex Nature of the contract.

2.2 Project Flight Planning

The contractor is responsible for all necessary flight planning, including, but not limited to determination of exposure locations, altitudes, and flight directions, required to acquire the imagery. See section C-5.2, Flight Planning of the contract.

2.3 Imagery Acquisition

Digital acquisitions require the Contractor to comply with the technical requirements and specifications of this contract, and Attachment A: Specification for Digital Camera Based Acquisition which defines the essential elements in securing high quality direct digital imagery. The digital system shall be a tested, stable, geometrically calibrated system with appropriate documentation, suitable for use in the acquisition and production of precision photogrammetric orthoimagery, and in accordance with NAIP contract requirements.

2.4 Priorities for Project Item Areas

The Contracting Officer or Contracting Officer Representative (COR) may direct, by written order, certain project item areas or regions within those areas listed under a Contract Award Item to be acquired in a priority order, weather and ground conditions permitting. All reasonable effort will be directed toward providing a schedule of operations favorable to both the Government and Contractor.

2.5 General Requirements

The Contractor shall provide digital ortho-rectified imagery in accordance with the requirements specified in the following table.

STATE	GROUND SAMPLE DISTANCE	COLOR TYPE ¹	ACQ PERIOD (2012)
Alabama	1-meter	4B	15 Jun - 15 Sep
Arizona*	1-meter	4B	1 Jun - 31 Aug*
Arkansas*	1-meter	4B	15 Jun - 15 Sep*
California	1-meter	4B	15 Apr - 7 Aug (4)
Colorado	1-meter	4B	1 Jul - 15 Sep (2)
Connecticut	1-meter	4B	1 Jul - 15 Aug
Delaware	1-meter	4B	15 Jun - 15 Aug
Florida	1-meter	4B	15 Apr - 31 Oct (3)

Georgia	1-meter	4B	25 Jun - 1 Sep
Idaho*	1-meter	4B	10 Jun - 15 Aug*
Illinois	1-meter	4B	1 Jun - 31 Jul (2)
Indiana	1-meter	4B	15 Jun - 15 Aug
Iowa	1-meter	4B	1 Jul - 15 Sep
Kansas	1-meter	4B	15 Jun - 1 Sep (2)
Kentucky	1-meter	4B	15 Jun - 15 Aug
Louisiana*	1-meter	4B	1 May - 31 Jul*
Maine	1-meter	4B	1 Jul - 15 Sep
Maryland*	1-meter	4B	1 Jun - 15 Aug*
Massachusetts	1-meter	4B	1 Jul - 31 Aug
Michigan*	1-meter	4B	17 Jun - 12 Aug*
Minnesota	1-meter	4B	1 Jun - 31 Aug
Mississippi	1-meter	4B	15 Jun - 31 Aug
Missouri	1-meter	4B	15 Jun - 31 Jul
Montana	1-meter	4B	15 Jun - 15 Aug (4)
Nebraska	1-meter	4B	1 Jul - 31 Aug
Nevada	1-meter	4B	1 Jun - 1 Aug
New Hampshire	1-meter	4B	1 Jul - 31 Aug
New Jersey	1-meter	4B	1 Jul - 31 Aug
New Mexico	1-meter	4B	15 May - 15 Aug
New York*	1-meter	4B	1 May - 30 Sep*
North Carolina	1-meter	4B	15 May - 15 Aug
North Dakota*	1-meter	4B	20 Jun - 20 Aug*
Ohio*	1-meter	4B	1 Jun - 1 Sep*
Oklahoma*	1-meter	4B	15 Apr - 30 Sep (2)*
Oregon	1-meter	4B	15 Jun - 15 Aug (2)
Pennsylvania*	1-meter	4B	1 May - 30 Sep*
Rhode Island	1-meter	4B	1 Jul - 15 Aug
South Carolina	1-meter	4B	15 Apr - 1 Jul
South Dakota*	1-meter	4B	1 Jul - 31 Aug*
Tennessee	1-meter	4B	1 Apr - 15 Sep (2)
Texas	1-meter	4B	15 Apr - 30 Sep (4)
Utah	1-meter	4B	15 Jun - 15 Aug
Vermont	1-meter	4B	1 Jul - 31 Aug
Virginia	1-meter	4B	15 Apr - 15 Aug (2)
Washington	1-meter	4B	15 Jun - 15 Sep (3)
West Virginia	1-meter	4B	1 Jul - 30 Sep
Wisconsin*	1-meter	4B	20 Jun - 31 Aug*
Wyoming*	1-meter	4B	1 Jul - 15 Aug*

Legend: * A non-contractual flying preference has been requested by the state (see map in Attachment 2)

¹ NC = Natural color; CIR = Color near-infrared, or 4B = 4-band multi-spectral

3.0 GOVERNMENT-FURNISHED PROPERTY

Pursuant to the Government-Furnished Property (GFP) clause (see Contract Section I-9, Clauses Incorporated by Reference) the Government shall furnish the items of property, in addition to items identified in the contract, listed below as GFP to the Contractor.

3.1 Metadata Template

The Contractor will be furnished upon award three (3) data text files (.txt) containing Federal Geographic Data Committee (FGDC) compliant metadata template to be used when creating the CCM metadata (as required in Section C-6.3(f)(1), Mosaic Metadata) and creating the county-based and state-based shapefile metadata (as required in paragraph 6.3(f)(3), Seamline Shapefile Metadata, and 6.2(h)(3), Metadata, respectfully).

3.2 Required Coverage

The Contractor will be furnished upon award one (1) Esri® compatible shapefile containing the required contract coverage. The shapefile contains, at a minimum, the following attributes: USGS Geographic Name Information System (GNIS) quad name, latitude and longitude of the southeast corner (expressed in both decimal degrees and degrees, minutes, seconds), and UTM zone.

3.3 State Project Area – DOQQ List

The Contractor will be furnished upon award one (1) data text file (.txt) containing a list of all Digital Ortho Quarter Quadrangles (DOQQ) tiles required for complete physical coverage of that state project area. The data text file will contain quad name, quadrant, state, latitude and longitude of the SE corner of the quad, USGS quad number, NAPP station number, latitude and longitude of the quad center, USDA arckey number, flying height AGL (for reference only), and the native UTM zone. The following is a sample of the data:

```

“AZTEC SE”,“SW”,“AZ”,“324500N”,“1131845W”,“3211314”,“1133W-0282”,
“32-46-53N”,“113-20-38W”,“3245001131845”,20000,12
“AZTEC SE”,“NW”,“AZ”,“324845N”,“1131845W”,“3211314”,“1133W-0284”,
“32-5038N”,“113-20-38W”,“3245001131845”,20000,12
“CALIENTE”,“SW”,“AZ”,“325230N”,“1131845W”,“3211306”,“1133W-0286”,
“32-454-23N”,“113-20-38W”,“3252301131845”,20000,12

```

3.4 Compressed County Mosaic (CCM) Coverage – DOQQ List

The Contractor will be furnished upon award one (1) data text file (.txt) containing a list of all DOQQ tiles required for the creation of the CCM coverage for each county in that state project. The data text file will contain the same information and same format as the state list above (paragraph 3.3, State Project Area – DOQQ List). All CCMs shall be projected in the NAD83 UTM zone listed in this data file.

3.0 ADMINISTRATIVE MATTERS

3.1 Annual Representations and Certifications

Contractors shall complete electronic annual representations and certifications at <http://orca.bpn.gov> in conjunction with the required registration in the Central Contractor Registration (CCR) database. Contractors shall submit updates to the Online Representations and Certifications Application (ORCA) as necessary, but at least annually, to ensure they are kept current, accurate, and complete. The representations and certifications are effective until one year from the date of submission or update to ORCA. Please refer to Section K-1, Annual Representations and Certifications, FAR Clause 52.204-8 of the contract.

3.2 Small Business Subcontracting Plan

If applicable, all Contractors, except those certified as a small business concern, shall submit a subcontracting plan that separately addresses subcontracting with small business, veteran-owned small business, service-disabled veteran-owned small business, HUBZone small business concerns, small disadvantaged business and women owned small business concerns. The subcontracting plan shall be included and made a part of the resultant task order award and be negotiated with the Contracting Officer during the task order negotiation period. Failure to submit and negotiate the subcontracting plan shall make the offeror ineligible for award. Please refer to Section I-9, Clauses Incorporated by Reference, Small Business Subcontracting Plan, FAR Clause 52.219-09 of the contract.

3.3 Task Order Ombudsman

The Director of USDA-FSA-Aerial Photography Field Office shall serve as the Task Order Ombudsman and is responsible for reviewing complaints from the contractors and ensuring that all of the contractors are afforded a fair opportunity to be considered for task orders issued under this contract. The Task Order Ombudsman may be contacted at telephone (801) 844-2907, or mail to: Director, APFO, 2222 West 2300 South, Salt Lake City, UT 84119.

3.4 Availability of Funds (FAR 52.232-18, April 1984)

Funds are not presently available for this contract. The Government's obligation under this contract is contingent upon the availability of appropriated funds from which payment for contract purposes can be made. No legal liability on the part of the Government for any payment may arise until funds are made available to the Contracting Officer for this contract and until the Contractor receives notice of such availability, to be confirmed in writing by the Contracting Officer.

LIST OF ATTACHMENTS

<u>Exhibit</u>	<u>Description</u>	<u>Page</u>
Exhibit 1	State Data Table	10
Exhibit 2	Required Documentation (3 Pages)	11-13
Attachment 1:	County Coverage Data (xx pages)	
Attachment 2:	State Coverage Maps (xx pages)	

DRAFT

EXHIBIT 1
State Data Table

STATE	NO. of COs	AREA (SQ MI)	DOQQs	NO. of EXP*
Alabama	67	54,531	3,482	7,037
Arizona	15	117,442	7,629	15,367
Arkansas	75	55,030	3,600	7,290
California	58	164,891	11,095	22,412
Colorado	64	107,651	7,423	14,959
Connecticut	8	5,754	412	856
Delaware	3	2,550	176	368
Florida	67	64,680	3,954	8,071
Georgia	159	61,440	3,913	7,912
Idaho	44	87,516	6,554	13,223
Illinois	102	59,028	4,131	8,348
Indiana	92	38,478	2,689	5,436
Iowa	99	58,733	4,239	8,592
Kansas	105	86,212	5,902	11,927
Kentucky	120	43,364	2,930	5,987
Louisiana	64	51,408	3,233	6,688
Maine	16	3,082	2,748	5,572
Maryland	24	13,138	906	1,898
Massachusetts	14	10,307	744	1,567
Michigan	83	64,595	4,844	9,942
Minnesota	87	87,625	6,791	13,742
Mississippi	82	50,792	3,237	6,550
Missouri	115	73,386	5,018	10,160
Montana	56	150,237	11,776	23,754
Nebraska	93	78,998	5,625	11,392
Nevada	17	107,377	7,454	15,040
New Hampshire	10	10,425	771	1,578
New Jersey	21	9,064	636	1,312
New Mexico	33	123,439	8,028	16,154
New York	62	53,073	3,880	7,921
North Carolina	100	54,382	3,581	7,333
North Dakota	53	72,238	5,712	11,546
Ohio	88	43,416	3,049	6,170
Oklahoma	77	73,061	4,815	9,769
Oregon	36	100,520	7,466	15,071
Pennsylvania	67	47,248	3,343	6,788
Rhode Island	5	1,619	116	248
South Carolina	46	33,308	2,154	4,387
South Dakota	66	79,962	5,992	12,114
Tennessee	95	45,364	3,000	6,142
Texas	254	274,703	17,277	34,783
Utah	29	87,040	6,032	12,145
Vermont	14	10,901	812	1,665
Virginia	100	44,857	3,029	6,212
Washington	39	72,408	5,718	11,578
West Virginia	55	26,664	1,831	3,745
Wisconsin	72	59,640	4,484	9,088
Wyoming	23	100,582	7,357	14,827

* Exposures are based on NAPP specification (i.e. 1:40,000 scale) and are provided for reference only

EXHIBIT 2
Required Documentation

1.0 AIRCRAFT TO BE USED IN COMPLETION OF ITEM(S) IN THIS ORDER

In the space provided below, list all aircraft proposed for use on this task order.

Aircraft Make/Model	Registration No. (Tail No.)	Operating Ceiling	Offeror Owned (check appropriate block)
			<input type="checkbox"/> Yes <input type="checkbox"/> No *
			<input type="checkbox"/> Yes <input type="checkbox"/> No *
			<input type="checkbox"/> Yes <input type="checkbox"/> No *
			<input type="checkbox"/> Yes <input type="checkbox"/> No *
			<input type="checkbox"/> Yes <input type="checkbox"/> No *
			<input type="checkbox"/> Yes <input type="checkbox"/> No *

* If the aircraft is/are not offeror owned, a written statement of availability from the owner of the aircraft must be enclosed. See Section C-4, Equipment Requirements.

2.0 CAMERA(S) TO BE USED IN COMPLETION OF ITEM(S) IN THIS ORDER

In the space provided below, list all cameras proposed for use on this task order. Current calibration report(s) must be enclosed or on file at the Aerial Photography Field Office.

Calibration Report Number	Make/Model	Serial Number	Offeror Owned (check appropriate block)
			<input type="checkbox"/> Yes <input type="checkbox"/> No *
			<input type="checkbox"/> Yes <input type="checkbox"/> No *
			<input type="checkbox"/> Yes <input type="checkbox"/> No *
			<input type="checkbox"/> Yes <input type="checkbox"/> No *
			<input type="checkbox"/> Yes <input type="checkbox"/> No *
			<input type="checkbox"/> Yes <input type="checkbox"/> No *

* If the camera(s) is/are not offeror owned, a written statement of availability from the owner(s) of the camera(s) must be enclosed. See Section C-4, Equipment Requirements.

3.0 KEY PERSONNEL INTENDED FOR PERFORMANCE ON THIS ORDER

List all key professional and technical personnel intended to perform on this task order. List may include project manager, pilot(s), photographer(s), and key back-up or support personnel.

Name	Title	Education	Years of Experience

4.0 INCOMPLETE CONTRACTS AS OF DATE OF PROPOSAL

In the space provided below, the Contractor is requested to indicate the remaining work that may coincide or conflict with the work proposed in this task order.

<i>Indicate by Linear Miles</i>	Remaining Work - Winter	Remaining Work - Summer
U.S. Government Contracts		
All Other Contracts		

5.0 DIGITAL CAMERA APPROVAL REQUIREMENTS

Each offeror proposing to use a digital camera shall have on file with the Aerial Photography Field Office (APFO), or shall submit camera documentation for approval. Please refer to Contract Attachment A, Paragraph 4, Digital Camera Approval Requirements, for digital camera approval requirements.

For each digital camera proposed to be used, please indicate which statement is correct:

- Digital Camera Approval Requirements on file at APFO.
- Digital Camera Approval Requirements submitted with offer.

7.0 CURRENT FINANCIAL STATEMENT

Offerors may be required to provide a "current" financial statement. For purposes of this solicitation, a current financial statement would be the most recent annual report, updated, if necessary, so that information reflects the company's financial status over the past 6 months.

All data shall be certified by an authorized company officer as to its accuracy and veracity or be validated by an independent certified public accountant. If necessary, the Contracting Officer may request additional financial information.

Financial information received will be treated as confidential and will not be used for purposes other than evaluation of financial responsibility. Failure to provide this information may delay or prohibit the Contracting Officer from making an affirmative decision on the offeror's responsibility. Please indicate which statement is correct:

- Current financial statement on file at APFO.
- Current financial statement submitted with offer.

**ATTACHMENT 1
COUNTY COVERAGE DATA**

STATE: California
 ACQ PERIOD: Multi-season (see Atch 2)
 TOTAL STATE DOQQs: 11,095
 COUNTIES: 58

COUNTY NAME	FIPS COD	QQs	UTM ZON
Alameda	6001	81	10
Alpine	6003	74	11
Amador	6005	67	10
Butte	6007	153	10
Calaveras	6009	99	10
Colusa	6011	113	10
Contra Costa	6013	79	10
Del Norte	6015	95	10
El Dorado	6017	155	10
Fresno	6019	483	11
Glenn	6021	111	10
Humboldt	6023	301	10
Imperial	6025	321	11
Inyo	6027	775	11
Kern	6029	574	11
Kings	6031	121	11
Lake	6033	130	10
Lassen	6035	381	10
Los Angeles	6037	335	11
Madera	6039	187	11
Marin	6041	65	10
Mariposa	6043	131	10
Mendocino	6045	294	10
Merced	6047	167	10
Modoc	6049	350	10
Mono	6051	266	11
Monterey	6053	275	10
Napa	6055	76	10
Nevada	6057	96	10
Orange	6059	74	11
Placer	6061	141	10
Plumas	6063	231	10
Riverside	6065	552	11
Sacramento	6067	99	10
San Benito	6069	124	10
San Bernardino	6071	1396	11
San Diego	6073	314	11
San Francisco	6075	15	10
San Joaquin	6077	127	10
San Luis Obispo	6079	265	10

San Mateo	6081	56	10
Santa Barbara	6083	233	10
Santa Clara	6085	114	10
Santa Cruz	6087	50	10
Shasta	6089	311	10
Sierra	6091	89	10
Siskiyou	6093	529	10
Solano	6095	90	10
Sonoma	6097	143	10
Stanislaus	6099	134	10
Sutter	6101	64	10
Tehama	6103	256	10
Trinity	6105	277	10
Tulare	6107	365	11
Tuolumne	6109	197	10
Ventura	6111	162	11
Yolo	6113	92	10
Yuba	6115	67	10

Sample 2011 Data

ATTACHMENT 2

STATE COVERAGE MAPS


NATIONAL


COVERAGE & PRIORITIES MAP	2
FLYING SEASON MAP	3

STATE

ALABAMA	4	NEW HAMPSHIRE	36
ARIZONA	5	NEW JERSEY	37
ARKANSAS	6	NEW MEXICO	38
CALIFORNIA	7	NEW YORK	39
CALIFORNIA SEASONS	8	NORTH CAROLINA	40
COLORADO	9	NORTH DAKOTA	41
COLORADO SEASONS	10	OHIO	42
CONNECTICUT	11	OKLAHOMA	43
DELAWARE	12	OKLAHOMA SEASONS	44
FLORIDA	13	OREGON	45
FLORIDA SEASONS	14	OREGON SEASONS	46
GEORGIA	15	PENNSYLVANIA	47
IDAHO	16	RHODE ISLAND	48
ILLINOIS	17	SOUTH CAROLINA	49
ILLINOIS SEASONS	18	SOUTH DAKOTA	50
INDIANA	19	TENNESSEE	51
IOWA	20	TENNESSEE SEASONS	52
KANSAS	21	TEXAS	53
KANSAS SEASONS	22	TEXAS SEASONS	54
KENTUCKY	23	UTAH	55
LOUISIANA	24	VERMONT	56
MAINE	25	VIRGINIA	57
MARYLAND	26	VIRGINIA SEASONS	58
MASSACHUSETTS	27	WASHINGTON	59
MICHIGAN	28	WASHINGTON SEASONS	60
MINNESOTA	29	WEST VIRGINIA	61
MISSISSIPPI	30	WISCONSIN	62
MISSOURI	31	WYOMING	63
MONTANA	32		
MONTANA SEASONS	33		
NEBRASKA	34		
NEVADA	35		

Sample 2011 Data

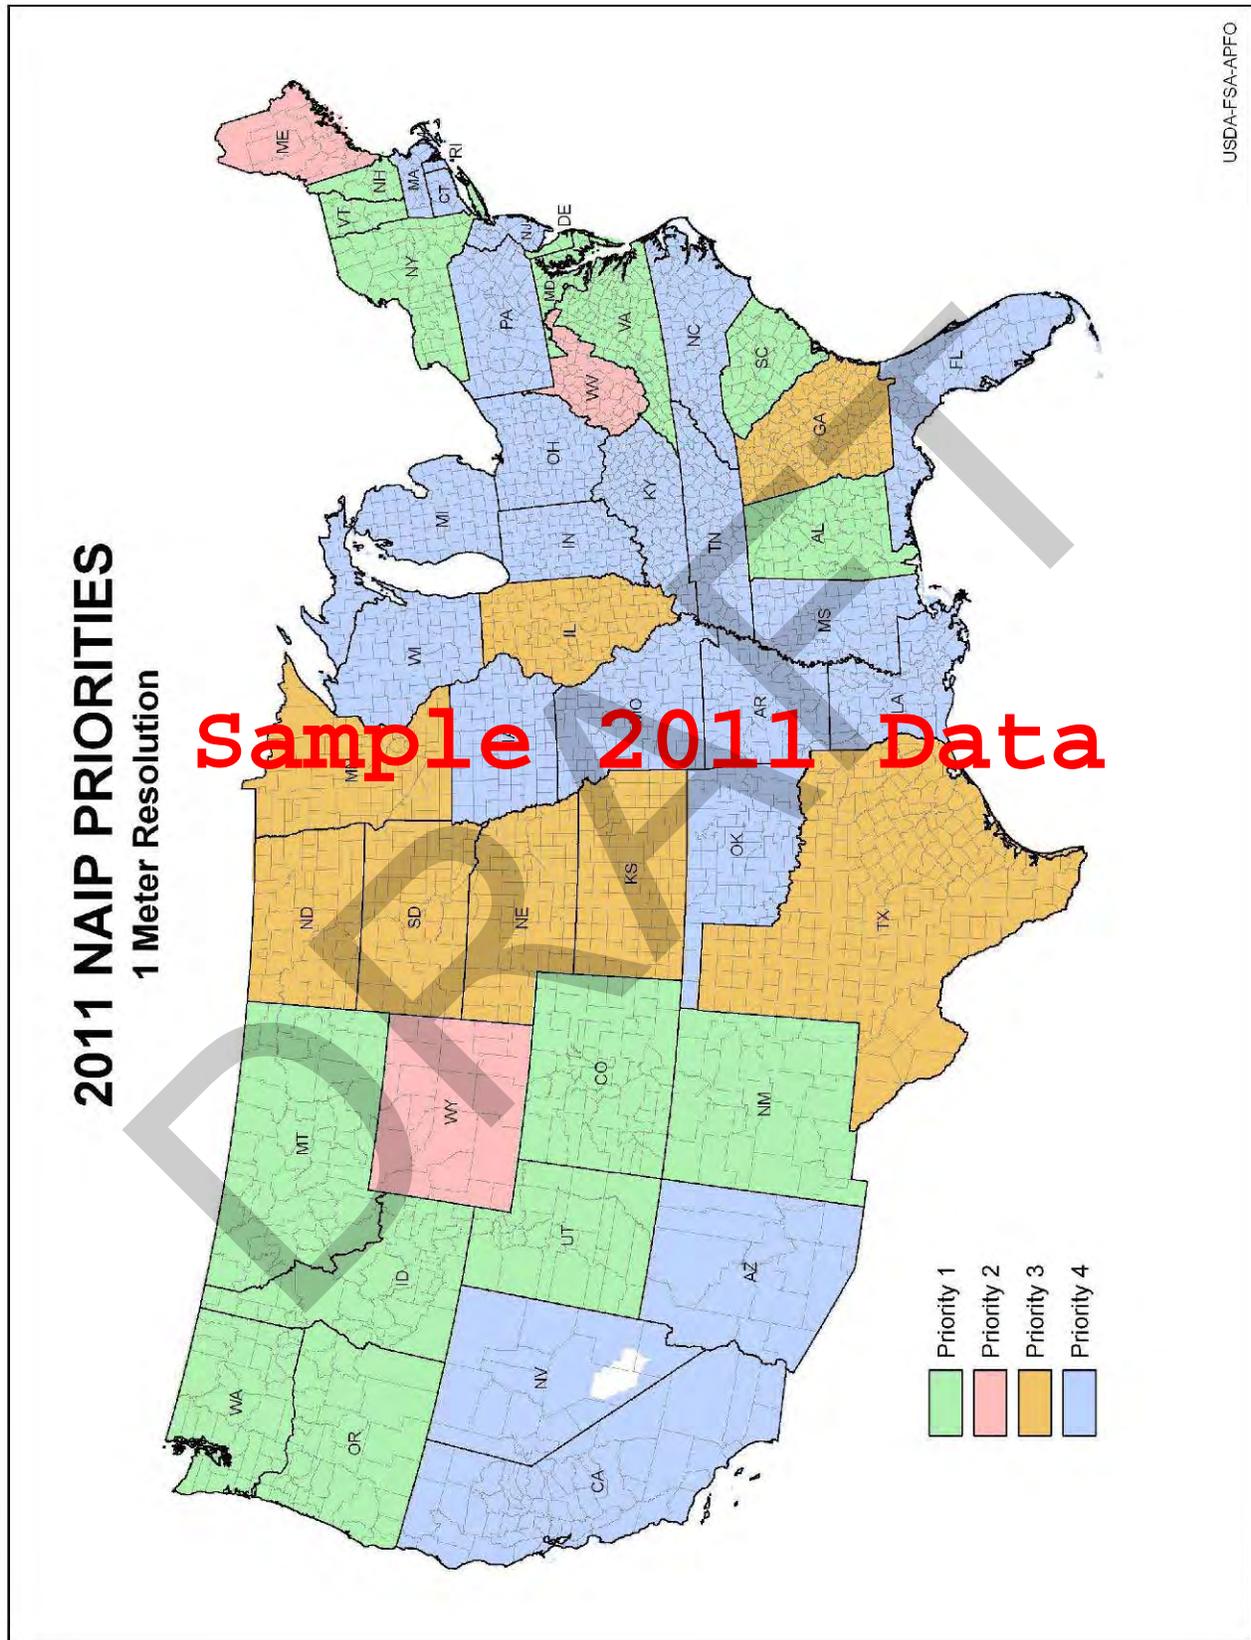

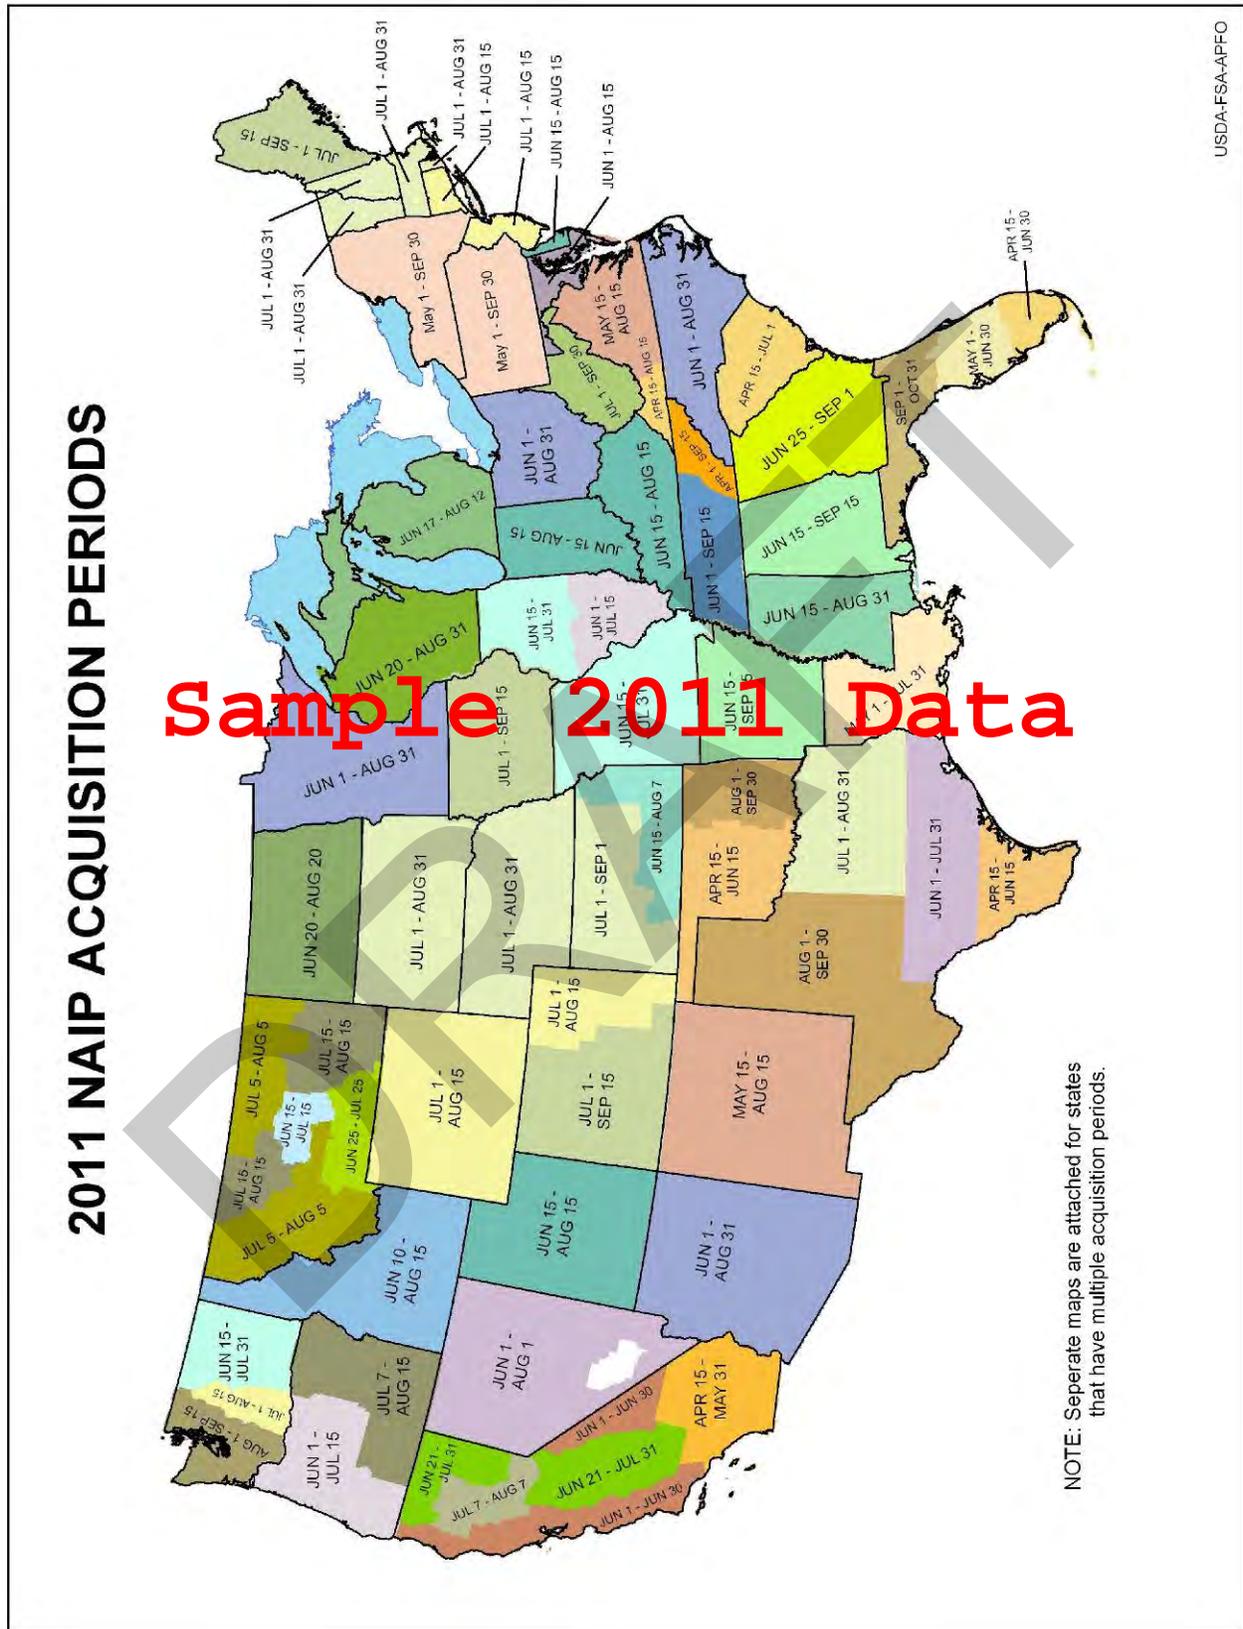

2011 State Project Map CALIFORNIA

Project Totals
Number of Counties - 58
Number of Photo Stations - 22,412
Number of DOQQs - 11,095
Square Miles - 164,891

Sample 2011 Data

-  County Boundary
-  DOQQs
-  MOA Areas
-  Restricted Areas

